



Measure S Program Update

January 16, 2019

Dave Rivera, Assistant Superintendent/CBO
Scott Harvey, Senior Executive Director, Administrative Services
Rory Lorenzo, Bond Program Manager




Orange High School

"ONCE A PANTHER, ALWAYS A PANTHER"

Budget: Status Unchanged at \$52,338,588

Schedule: Construction Underway –
Framing and Utilities

- ❖ Science Center-
- ❖ Contract: Pinner Construction - **\$26,109,000**
- ❖ Change Orders (1 total):
CO#1: \$77,284 (BA 12/19/19)

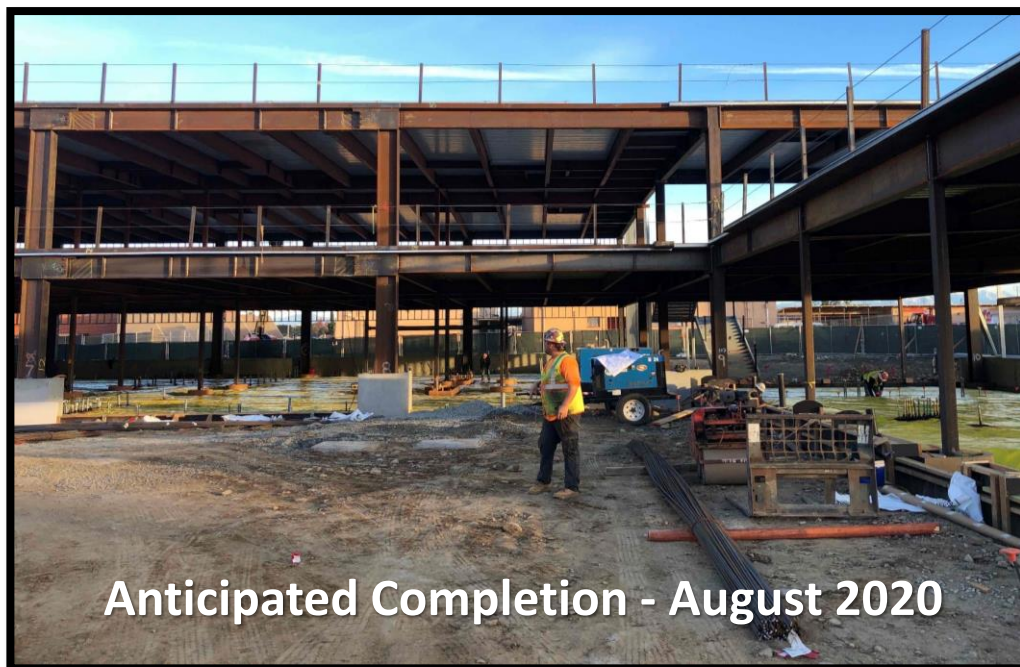

New STEM Building (42,300 sq. ft.)

- 12 Laboratory Room
- 1 General Classroom
- 2 Medically Fragile Classrooms





Orange High School

"ONCE A PANTHER, ALWAYS A PANTHER"

Budget: Status Unchanged at \$52,338,588

Schedule: Construction Underway





VILLA PARK HIGH SCHOOL

Budget: Status Unchanged at \$43,200,000

**Schedule: Status Construction Underway -
Structural Steel/Underground Utilities**

Anticipated Completion – November 2020

New STEM Building (47,136 sq. ft.)

- 12 Laboratory Rooms
- 2 General Classroom
- 2 Medically Fragile Classrooms



❖ **Science Center:**

Contract: Angeles Contractor - **\$23,997,000**

Change Orders (4 total & 1 Credit):

CO#1: \$2,806 (BA 3/14/19)

CO#2: \$8,127 Credit (BA 10/17/19)

CO#3: \$63,960 (BA 10/17/19)

CO#4: \$5,397 (BA 12/19/19)





VILLA PARK HIGH SCHOOL

Budget: Status Unchanged at \$43,200,000

Schedule: Construction Underway





EL MODENA HIGH SCHOOL

Budget: Reduced to \$37,065,655

Schedule: Construction Underway –
Structural Steel



New STEM Building (42,501 sq. ft.)

- 12 Laboratory Rooms
- 1 General Classroom
- 2 Medically Fragile Classrooms

❖ Science Center:

Contract: Angeles Contractor - **\$25,818,000**

❖ ***NO CURRENT CHANGE ORDERS***





EL MODENA HIGH SCHOOL

Budget: Reduced to \$37,065,655

Schedule: Construction Underway





CANYON HIGH SCHOOL
HOME OF THE COMANCHES

Budget: Status Unchanged at \$69,500,000

Schedule: **Construction Underway - Interim**
Kitchen Complete/Electrical Infrastructure



Anticipated Completion – April 2021

New STEM Building (61,419 sq. ft.)

- 12 Laboratory Rooms
- 12 General Classrooms
- Student Services, Counseling & Administration
- New Food Services (Remodel of Admin. Bldg.)
- Infrastructure Upgrades

Contract: Swinerton Builders- \$38,400,000

❖ NO CURRENT CHANGE ORDERS





CANYON HIGH SCHOOL
HOME OF THE COMANCHES

Budget: Status Unchanged at \$69,500,000

Schedule: **Construction Underway**





PHASE II UPDATE (Updated Tentative Schedule)



Design Contracts Approved: July 25, 2019

- **Schematic Design:** October 2019 – January 2019
- **Design Development:** January 2020 – April 2020
- **PRESENTATION TO BOARD:** May/June 2020
- **Construction Documents:** June 2020 – September 2020
- **DSA Review:** September 2020 – February 2021
- **Procurement:** March 2021 – May 2021
- **Construction:** May 2021- May 2023





Questions?
