



Measure S Board Meeting Update

October 17, 2019

Dave Rivera, Assistant Superintendent/CBO
Scott Harvey, Senior Executive Director, Administrative Services
Rory Lorenzo, Bond Program Manager



PROGRAM HIGHLIGHTS & MILESTONES

- ☒ DSA approval for ALL Measure S Phase I Projects: Completed January 31, 2019
- ☒ California Environmental Quality Act (CEQA) approval has been received for ALL Measure S Phase I Projects
- ☒ All construction bids received and authorized for Science Center projects by May 9, 2019



Orange High School


"ONCE A PANTHER, ALWAYS A PANTHER"

Budget Status: Unchanged at \$52,338,588

Schedule Status: Science Center Underway



NEW SNACK BAR

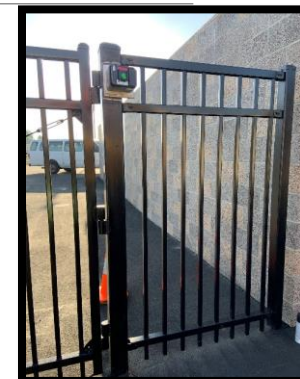

NEW BUS PICK-UP/DROP OFF



NEW ELECTRICAL YARD

- ❖ Infrastructure Upgrades- Completed
Contract: Swinerton Builders - \$5,965,424
Change Orders (5 total): \$591,004



Orange High School

"ONCE A PANTHER, ALWAYS A PANTHER"

Budget Status: Unchanged at \$52,338,588

Schedule Status: Science Center Underway

- ❖ Science Center- **Structural Steel**
- ❖ Contract: Pinner Const.- **\$26,109,000**

New STEM Building (42,300 sq. ft.)

- 12 Laboratory Room
- 1 General Classroom
- 2 Medically Fragile Classrooms





Orange High School

"ONCE A PANTHER, ALWAYS A PANTHER"

Budget Status: Unchanged at \$52,338,588

Schedule Status: Science Center Underway





VILLA PARK HIGH SCHOOL

Budget Status: Unchanged at \$43,200,000

Schedule Status: Science Center Underway

Anticipated Completion – November 2020

New STEM Building (47,136 sq. ft.)

- 12 Laboratory Rooms
- 2 General Classroom
- 2 Medically Fragile Classrooms



❖ Science Center: **Structural Steel**

Contract: Angeles Contractor - **\$23,997,000**

Change Orders (3 total):

CO#1: \$2,806 (BA 3/14/19)

CO#2: \$8,127 Credit Proposed 10/17/19

CO#3: \$63,960 Proposed 10/17/19





VILLA PARK HIGH SCHOOL

Budget Status: Unchanged at \$43,200,000

Schedule Status: Science Center Underway





EL MODENA HIGH SCHOOL

Budget Status: Reduced to \$37,065,655

Schedule Status: Science Center Underway



New STEM Building (42,501 sq. ft.)

- 12 Laboratory Rooms
- 1 General Classroom
- 2 Medically Fragile Classrooms

❖ Science Center: **Final Grading, Structural Foundations**
Contract: Angeles Contractor - **\$25,818,000**





CANYON HIGH SCHOOL
HOME OF THE COMANCHES

Budget Status: **Unchanged at \$69,500,000**

Schedule Status: **Science Center Underway**



Anticipated Completion – April 2021

New STEM Building (61,419 sq. ft.)

- 12 Laboratory Rooms
- 12 General Classrooms
- Student Services, Counseling & Administration
- New Food Services (Remodel of Admin. Bldg.)
- Infrastructure Upgrades

Contract: Swinerton Builders- \$38,400,000

Interim Kitchen Final Stages





PHASE II UPDATE (Tentative Schedule)

- Design Contracts Approved: July 25, 2019
- Schematic Design: October 2019 – December 2019
- Design Development: December 2019 – February 2020
- **PRESENTATION TO BOARD:** March/April 2020
- Construction Documents: March 2020 – June 2020
- DSA Review: June 2020 – October 2020
- Procurement: November 2020 – January 2021
- Construction: February 2021- February 2023





Questions?
